


## **2018 Capital Improvement Program**

## **Program Dollar Value by Phase**



Project Phase	Project Count	Dollar Value
0-Not Started	88	\$130,151,986
1-Design	20	\$27,803,935
2-Bid-Award	27	\$33,011,055
3-Construction	69	\$249,657,424
4-Close Out	62	\$206,452,502
5-Complete	75	\$117,434,812
6-On Hold	0	\$0
7-Contingency	3	\$64,761,285
Totals	344	\$829,272,997

## **Program Narrative**

The 2018 Capital Improvement Program includes the 5B bond voted on and passed in November of 2018.

% of defined bond projects have been initiated as of March 2022.

	Occup	ancy Deadl	ines At-Risk	Finish	n Date	
Priority Facility N	Name	Project ID	Project name	Target	Forecast	

## **Program Contingency and Remaining Funds**

Program Contingency	Forecast Remaining	Net Remaining
(Unallocated)	Funds in Projects	Program Funds
\$64,761,285	(\$7,655,618)	

Report Date: 15-Mar-22 Page 1 of 11



# 2018 Capital Improvement Program - Project Detail

Fiscal Plan Year: 2023	Work Prog	gress		Вι	Budget Summary			
Project Description	Phase	%	Original	Current	Variance	Haz-Mat	Notes	
Charter New America School General Upgrades	Not Started	0%	\$0	\$640,682	\$640,682	\$0	PI	
	2023 Sub	2023 Subtotals:		\$640,682	\$640,682	\$0		

Fiscal Plan Year: 2022	Work Prog	gress		Bu	dget Summary	У			
Project Description	Phase	%	Original	Current	Variance	Haz-Mat	Notes		
Carmody MS Eff & Future Rdy 2nd Floor	Not Started	0%	\$0	\$100,000	\$100,000	\$0			
G DW Modular Bldg Removal 2022 7-ES 1-Other	Not Started	0%	\$0	\$350,000	\$350,000	\$0			
Charter Doral Academy New Site & School	Design	92%	\$3,090,152	\$3,730,804	\$640,652	\$0	PI		
Creighton MS Efficiency & Future Ready	Design	4%	\$876,001	\$876,001	\$0	\$0			
D'Evelyn Jr/Sr FF&E	Design	0%	\$0	\$180,000	\$180,000	\$0			
Elk Creek ES FF&E	Design	0%	\$0	\$288,312	\$288,312	\$0			
Evergreen MS FF&E	Design	0%	\$114,000	\$114,000	\$0	\$0			
G DW Elevator Upgrades 2022 1-ES 1-MS 1-HS	Design	100%	\$0	\$350,000	\$350,000	\$0			
G DW LED Lighting 2022 8-ES 2-MS 2-HS 3-Other	Design	4%	\$2,144,166	\$2,144,166	\$0	\$0			
G DW Paving 2022 5-ES 1-MS	Design	11%	\$1,135,050	\$1,135,050	\$0	\$0			
Jeffco Open School FF&E	Design	0%	\$9,660	\$70,000	\$60,340	\$0			
Marshdale ES FF&E	Design	0%	\$1,000,000	\$516,250	(\$483,750)	\$0			
North Arvada MS FF&E	Design	0%	\$735,000	\$262,500	(\$472,500)	\$0			
Peck ES FF&E	Design	0%	\$483,000	\$291,594	(\$191,406)	\$0			
Powderhorn ES FF&E	Design	0%	\$0	\$561,000	\$561,000	\$0	FFE		
Prospect Valley ES FF&E	Design	0%	\$401,409	\$684,250	\$282,841	\$0			
Ralston Valley HS FF&E	Design	0%	\$0	\$406,875	\$406,875	\$0			
Standley Lake HS FF&E	Design	0%	\$1,377,600	\$1,399,897	\$22,297	\$0			
Vanderhoof ES FF&E	Design	0%	\$0	\$117,469	\$117,469	\$0			
Wheat Ridge HS Efficiency & Future Ready	Design	2%	\$13,848,732	\$13,848,732	\$0	\$0			
Wilmore-Davis ES FF&E	Design	0%	\$218,850	\$258,806	\$39,957	\$0			
Arvada West HS Efficiency & Future Ready	Bid-Award	12%	\$1,038,715	\$1,038,715	\$0	\$0			
Bear Creek High HS Efficiency & Future Ready	Bid-Award	10%	\$1,138,341	\$1,138,341	\$0	\$0			
Bergen Valley ES Efficiency & Future Ready	Bid-Award	8%	\$277,506	\$277,506	\$0	\$0			
Blue Heron ES Efficiency & Future Ready	Bid-Award	11%	\$489,889	\$489,889	\$0	\$0			
Colorow ES Efficiency & Future Ready	Bid-Award	8%	\$1,876,115	\$1,813,115	(\$63,000)	\$0			
Fairmount Mechanical & LED Upgrades 1-ES	Bid-Award	8%	\$1,277,409	\$1,277,409	\$0	\$0			
G DW Flooring 2022-I 4-ES 3-MS	Bid-Award	15%	\$1,720,830	\$1,981,832	\$261,002	\$0			
G DW Playground 2022-l 4-ES	Bid-Award	8%	\$514,500	\$514,500	\$0	\$0			
Green Mountain ES Efficiency & Future Ready	Bid-Award	10%	\$634,629	\$970,065	\$335,436	\$0			
Lakewood HS Efficiency & Future Ready	Bid-Award	12%	\$2,046,141	\$2,173,117	\$126,976	\$0			
Mandalay MS Efficiency & Future Ready	Bid-Award	30%	\$602,134	\$539,134	(\$63,000)	\$0			
Mortenson ES Efficiency & Future Ready	Bid-Award	8%	\$538,997	\$538,997	\$0	\$0			
Mt Evans OELS Efficiency & Future Ready	Bid-Award	6%	\$3,210,190	\$5,611,048	\$2,400,858	\$0	MC,UC,SC		
North Arvada MS Efficiency & Future Ready	Bid-Award	11%	\$2,392,923	\$2,392,923	\$0	\$0			
Peck ES Efficiency & Future Ready	Bid-Award	6%	\$276,140	\$276,140	\$0	\$0			
Secrest ES Efficiency & Future Ready	Bid-Award	5%	\$382,338	\$382,338	\$0	\$0			
Shaffer ES Efficiency & Future Ready	Bid-Award	13%	\$434,372	\$434,372	\$0	\$0			
Slater ES Efficiency & Future Ready	Bid-Award	9%	\$1,262,059	\$1,375,059	\$113,000	\$0			
Stevens ES Efficiency & Future Ready	Bid-Award	8%	\$624,688	\$754,932	\$130,244	\$0			
Stony Creek ES Efficiency & Future Ready	Bid-Award	9%	\$736,204	\$736,204	\$0	\$0			
Thomson ES Efficiency & Future Ready	Bid-Award	6%	\$664,090	\$996,782	\$332,692	\$0			

Report Date: 15-Mar-22 Page 2 of 11



Fiscal Plan Year: 2022	Work Prog	ress		Bu	dget Summary	1	
Project Description	Phase	%	Original	Current	Variance	Haz-Mat	Notes
Ute Meadows ES Efficiency & Future Ready	Bid-Award	8%	\$794,084	\$794,084	\$0	\$0	
Warder ES Efficiency & Future Ready	Bid-Award	16%	\$481,102	\$544,102	\$63,000	\$0	
Warren Tech North Efficiency & Future Ready	Bid-Award	15%	\$425,202	\$425,202	\$0	\$0	
Westgate ES Efficiency & Future Ready	Bid-Award	6%	\$1,094,042	\$1,094,042	\$0	\$0	
Wilmore Davis ES Efficiency & Future Ready	Bid-Award	7%	\$1,100,225	\$1,100,225	\$0	\$0	
Windy Peak OELS Efficiency & Future Ready	Bid-Award	10%	\$3,340,982	\$3,340,982	\$0	\$0	
Charter Rocky Mtn Academy Evergreen General Upgrades	Construction	75%	\$0	\$640,682	\$640,682	\$0	PI
Charter Woodrow Wilson Academy General Upgrades	Construction	64%	\$0	\$640,877	\$640,877	\$0	PI
Elk Creek ES Efficiency & Future Ready	Construction	7%	\$590,686	\$733,000	\$142,314	\$0	
Emory ES Efficiency & Future Ready	Construction	8%	\$2,261,031	\$2,261,031	\$0	\$0	
G DW Flooring 2022-II 7-ES	Construction	5%	\$1,460,855	\$1,460,855	\$0	\$0	
G DW Mechanical 2022 3-ES	Construction	9%	\$4,597,740	\$4,597,740	\$0	\$0	
G DW Network Upgrades 2022 75-ES 13-MS 12-HS 18-Other	Construction	28%	\$0	\$14,600,000	\$14,600,000	\$0	BD
G DW Playground 2022-II 2-ES	Construction	11%	\$147,000	\$387,397	\$240,397	\$0	
G DW Roofing 2022 4-ES 1-MS	Construction	6%	\$2,850,746	\$2,850,746	\$0	\$0	
G DW Security Glass 2022 7-ES 1-MS 1-HS 1-Other	Construction	10%	\$72,000	\$72,000	\$0	\$0	
Golden HS Efficiency & Future Ready	Construction	11%	\$535,812	\$535,812	\$0	\$0	
Long View HS Efficiency & Future Ready	Construction	15%	\$240,710	\$384,869	\$144,159	\$0	
Mitchell ES Efficiency & Future Ready	Construction	5%	\$558,434	\$886,096	\$327,663	\$0	
Red Rocks ES Efficiency & Future Ready	Construction	8%	\$1,260,562	\$1,210,562	(\$50,000)	\$0	
Shelton ES Efficiency & Future Ready	Construction	9%	\$1,309,323	\$1,309,323	\$0	\$0	
West Jeff ES Efficiency & Future Ready	Construction	7%	\$178,130	\$178,130	\$0	\$0	
Swanson ES Playground Upgrades	Close Out	100%	\$175,000	\$178,679	\$3,679	\$0	
	2022 Subt	otals:	\$71,045,496	\$93,624,562	\$22,579,066	\$0	

Fiscal Plan Year: 2021	Work Prog	ress	Budget Summary				
Project Description	Phase	%	Original	Current	Variance	Haz-Mat	Notes
Alameda Int'l Jr-Sr HS FF&E	Construction	87%	\$378,000	\$933,750	\$555,750	\$0	FFE
Bell MS FF&E	Construction	78%	\$225,000	\$926,614	\$701,614	\$0	FFE
Carmody MS FF&E	Construction	95%	\$94,500	\$416,730	\$322,230	\$0	
Charter Compass Montessori Golden General Upgrades	Construction	22%	\$0	\$640,682	\$640,682	\$0	PI
Charter Two Roads Arvada General Upgrades	Construction	28%	\$0	\$640,682	\$640,682	\$0	PI
Columbine HS FF&E	Construction	97%	\$1,470,000	\$1,317,326	(\$152,674)	\$0	
D'Evelyn Jr-Sr HS Addition	Construction	58%	\$870,082	\$6,262,085	\$5,392,003	\$0	SC,BD
Dennison ES FF&E	Construction	94%	\$42,840	\$548,918	\$506,078	\$0	FFE
Devinny ES FF&E	Construction	90%	\$105,000	\$344,865	\$239,865	\$0	
Evergreen HS Renovation & General Upgrades	Construction	34%	\$10,136,692	\$10,136,692	\$0	\$375,805	
Evergreen MS Renovation & Upgrades	Construction	53%	\$7,606,755	\$6,902,866	(\$703,889)	\$72,650	
Everitt MS Efficiency & Future Ready	Construction	99%	\$3,000,921	\$2,892,864	(\$108,057)	\$91,559	
Everitt MS FF&E	Construction	96%	\$297,500	\$280,187	(\$17,313)	\$0	
Fitzmorris ES FF&E	Construction	90%	\$110,250	\$329,112	\$218,862	\$0	
Foster ES FF&E	Construction	81%	\$498,750	\$329,808	(\$168,942)	\$0	
G DW Field Improvements 2021 1-ES 4-HS	Construction	95%	\$2,887,500	\$11,562,864	\$8,675,364	\$0	SC
G DW LED Lighting 2021 11-ES	Construction	98%	\$1,835,700	\$1,626,907	(\$208,793)	\$2,440	
G DW Mechanical 2021 5-ES	Construction	97%	\$2,924,250	\$4,128,260	\$1,204,010	\$81,480	SC
H DW Elevator Upgrades 2021 6-ES 7-MS 8-HS 4-Other	Construction	100%	\$0	\$311,086	\$311,086	\$0	
Jeffco Open School Efficiency & Future Ready	Construction	22%	\$9,700,287	\$11,651,147	\$1,950,860	\$187,125	MC
Jefferson Jr-Sr HS FF&E	Construction	86%	\$0	\$168,750	\$168,750	\$0	

Report Date: 15-Mar-22 Page 3 of 11



Fiscal Plan Year: 2021	Work Prog	gress		Bu	Budget Summary			
Project Description	Phase	%	Original	Current	Variance	Haz-Mat	Notes	
Kullerstrand ES Efficiency & Future Ready	Construction	98%	\$1,143,045	\$1,184,838	\$41,793	\$97,555		
Kullerstrand ES FF&E	Construction	100%	\$147,000	\$245,308	\$98,308	\$0		
Kyffin ES FF&E	Construction	90%	\$341,250	\$425,853	\$84,603	\$0		
Lasley ES FF&E	Construction	76%	\$441,000	\$192,668	(\$248,332)	\$0		
Lumberg ES FF&E	Construction	93%	\$551,250	\$516,577	(\$34,673)	\$0		
Manning School FF&E	Construction	39%	\$21,105	\$432,812	\$411,708	\$0		
Maple Grove ES FF&E	Construction	96%	\$194,250	\$299,543	\$105,293	\$0		
Marshdale ES Replace School	Construction	53%	\$20,000,000	\$18,174,140	(\$1,825,860)	\$82,115		
Miller Special School Efficiency & Future Ready	Construction	96%	\$1,616,366	\$1,682,016	\$65,650	\$4,947		
Parmalee ES FF&E	Construction	80%	\$168,000	\$177,381	\$9,381	\$0		
Pomona HS FF&E	Construction	69%	\$1,050,000	\$547,800	(\$502,200)	\$0		
Powderhorn ES Addition & General Upgrades	Construction	34%	\$5,876,860	\$5,876,860	\$0	\$15,600		
Prospect Valley ES Replace School	Construction	32%	\$20,000,000	\$20,570,925	\$570,925	\$0	MC	
Ralston Valley HS Addition & General Upgrades	Construction	16%	\$7,625,513	\$8,240,001	\$614,488	\$0	MC	
Ryan ES FF&E	Construction	91%	\$362,250	\$334,842	(\$27,408)	\$0		
Standley Lake HS Addition & General Upgrades	Construction	16%	\$8,033,020	\$8,033,020	\$0	\$0		
Allendale ES FF&E	Close Out	100%	\$365,872	\$71,409	(\$294,464)	\$0		
CTE South FF&E	Close Out	100%	\$500,000	\$199,432	(\$300,568)	\$0		
Carmody MS Efficiency & Future Ready	Close Out	99%	\$1,589,108	\$1,789,009	\$199,901	\$23,327		
Chatfield HS Efficiency & Future Ready	Close Out	97%	\$2,736,353	\$3,067,410	\$331,058	\$0		
Dakota Ridge HS Efficiency & Future Ready	Close Out	100%	\$3,162,502	\$3,179,401	\$16,899	\$0		
Deane ES Efficiency & Future Ready	Close Out	100%	\$847,878	\$609,560	(\$238,318)	\$12,521		
Dennison ES Efficiency & Future Ready	Close Out	97%	\$966,488	\$1,033,363	\$66,875	\$87,945		
Devinny ES Efficiency & Future Ready	Close Out	100%	\$745,596	\$954,282	\$208,686	\$15,009		
Fitzmorris ES Efficiency & Future Ready	Close Out	97%	\$1,059,436	\$998,240	(\$61,196)	\$20,910		
G DW Flooring 2021 6-ES	Close Out	100%	\$1,306,266	\$1,358,208	\$51,942	\$308,001		
5 DW Modular Bldg Removal 2021 5-ES	Close Out	100%	\$0	\$201,014	\$201,014	\$0		
G DW Paving 2021 3-ES 1-MS	Close Out	100%	\$682,500	\$636,135	(\$46,365)	\$0		
G DW Playgrounds 2021 9-ES	Close Out	99%	\$692,475	\$1,995,016	\$1,302,541	\$0	MC,SC	
G DW Roofing 2021 5-ES	Close Out	100%	\$1,887,929	\$1,659,341	(\$228,588)	\$0		
G DW Security Glass 2021 6-ES 5-MS 1-HS	Close Out	100%	\$96,000	\$96,000	\$0	\$0		
Golden HS Doors Replacement	Close Out	100%	\$263,486	\$257,443	(\$6,043)	\$0		
Green Mountain ES FF&E	Close Out	100%	\$38,663	\$135,741	\$97,077	\$0		
Jefferson Academy Charter Debt Repayment	Close Out	100%	\$0	\$1,281,894	\$1,281,894	\$0	PI	
Kyffin ES Efficiency & Future Ready	Close Out	96%	\$4,144,305	\$3,901,261	(\$243,044)	\$84,114		
Lasley ES Efficiency & Future Ready	Close Out	100%	\$632,859	\$639,300	\$6,441	\$11,149		
Lawrence ES Efficiency & Future Ready	Close Out	100%	\$2,443,566	\$2,111,172	(\$332,394)	\$0		
Maple Grove ES Efficiency & Future Ready	Close Out	100%	\$807,121	\$723,322	(\$83,799)	\$28,360	_	
Patterson Cottages Efficiency & Future Ready	Close Out	100%	\$360,591	\$258,407	(\$102,184)	\$28,458		
Patterson International Efficiency & Future Ready	Close Out	100%	\$526,229	\$597,682	\$71,452	\$32,212		
Ryan ES Efficiency & Future Ready	Close Out	100%	\$1,213,833	\$1,202,567	(\$11,266)	\$0		
Sheridan Green ES Efficiency & Future Ready	Close Out	100%	\$851,758	\$1,269,702	\$417,944	\$0		
Sheridan Green ES FF&E	Close Out	100%	\$473,550	\$173,067	(\$300,483)	\$0		
Stott ES Efficiency & Future Ready	Close Out	100%	\$826,580	\$878,397	\$51,818	\$87,872		
Vanderhoof ES Efficiency & Future Ready	Close Out	100%	\$1,707,668	\$2,140,122	\$432,455	\$134,165		
Wayne Carle MS FF&E	Close Out	100%	\$182,000	\$152,681	(\$29,319)	\$0		
Westridge ES Efficiency & Future Ready	Close Out	100%	\$418,174	\$457,776	\$39,602	\$0		
Allendale ES Efficiency & Future Ready	Complete	100%	\$752,628	\$60,252	(\$692,376)	\$0		
Slater ES Asbestos Abatement	Complete	100%	\$0	\$0	\$0	\$5,850		
	2021 Subt		\$142,036,351	\$165,266,554	\$21,339,036	\$1,891,167		

Report Date: 15-Mar-22 Page 4 of 11



Brady Exploration School Efficiency & Future Ready         Construction         99%         \$1,752,517         \$1,907,850         \$           Charter Compass Montessori Wheat Ridge General Upgrades         Construction         76%         \$3,090,152         \$2,651,099         (\$4           Charter Montessori Peaks Academy General Upgrades         Construction         76%         \$3,090,152         \$3,832,043         \$           Charter Rocky Mountain Deaf School General Upgrades         Construction         79%         \$3,090,152         \$3,828,328         \$           Foster ES Addition & General Upgrades         Construction         89%         \$5,364,815         \$5,420,595           H DW HVAC 2020         Construction         100%         \$1,926,540         \$2,082,157         \$           2-ES 1-Other         Construction         100%         \$7,027,183         \$7,437,932         \$           Manning School Addition & General Upgrades         Construction         99%         \$6,403,971         \$6,375,141         (\$           Parmalee ES Addition & General Upgrades         Construction         96%         \$3,571,423         \$4,145,345         \$	155,333 39,053) 741,891 738,176 \$55,780 \$20 155,617 \$: 410,749 28,829) \$:	\$0 \$0 \$0 \$0 \$0 \$0 03,716 35,165	CC,PI PI PI
Charter Compass Montessori Wheat Ridge General Upgrades         Construction         76%         \$3,090,152         \$2,651,099         (\$4           Charter Montessori Peaks Academy General Upgrades         Construction         76%         \$3,090,152         \$3,832,043         \$           Charter Rocky Mountain Deaf School General Upgrades         Construction         79%         \$3,090,152         \$3,828,328         \$           Foster ES Addition & General Upgrades         Construction         89%         \$5,364,815         \$5,420,595         \$           H DW HVAC 2020         Construction         100%         \$1,926,540         \$2,082,157         \$           2-ES 1-Other         Construction         100%         \$7,027,183         \$7,437,932         \$           Manning School Addition & General Upgrades         Construction         99%         \$6,403,971         \$6,375,141         (\$           Parmalee ES Addition & General Upgrades         Construction         96%         \$3,571,423         \$4,145,345         \$	39,053) 741,891 738,176 \$55,780 \$2( 155,617 \$3( 410,749 28,829) \$3	\$0 \$0 \$0 03,716 35,165	PI
Charter Montessori Peaks Academy General Upgrades         Construction         76%         \$3,090,152         \$3,832,043         \$           Charter Rocky Mountain Deaf School General Upgrades         Construction         79%         \$3,090,152         \$3,828,328         \$           Foster ES Addition & General Upgrades         Construction         89%         \$5,364,815         \$5,420,595           H DW HVAC 2020         Construction         100%         \$1,926,540         \$2,082,157         \$           2-ES 1-Other         Construction         100%         \$7,027,183         \$7,437,932         \$           75-ES 13-MS 12-HS 18-Other         Construction         99%         \$6,403,971         \$6,375,141         (\$           Manning School Addition & General Upgrades         Construction         96%         \$3,571,423         \$4,145,345         \$	741,891 738,176 \$55,780 \$20 155,617 \$3 410,749 28,829) \$3	\$0 \$0 03,716 35,165	PI
Charter Rocky Mountain Deaf School General Upgrades         Construction         79%         \$3,090,152         \$3,828,328         \$           Foster ES Addition & General Upgrades         Construction         89%         \$5,364,815         \$5,420,595           H DW HVAC 2020         Construction         100%         \$1,926,540         \$2,082,157         \$           2-ES 1-Other         Construction         100%         \$7,027,183         \$7,437,932         \$           H DW Network Upgrades         Construction         100%         \$7,027,183         \$7,437,932         \$           75-ES 13-MS 12-HS 18-Other         Construction         99%         \$6,403,971         \$6,375,141         (\$           Manning School Addition & General Upgrades         Construction         96%         \$3,571,423         \$4,145,345         \$	738,176 \$26 \$55,780 \$26 155,617 \$3 410,749 \$28,829) \$3	\$0 03,716 35,165	
Foster ES Addition & General Upgrades         Construction         89%         \$5,364,815         \$5,420,595           H DW HVAC 2020         Construction         100%         \$1,926,540         \$2,082,157         \$           2-ES 1-Other         Construction         100%         \$7,027,183         \$7,437,932         \$           H DW Network Upgrades 75-ES 13-MS 12-HS 18-Other         Construction         100%         \$7,027,183         \$7,437,932         \$           Manning School Addition & General Upgrades         Construction         99%         \$6,403,971         \$6,375,141         (\$           Parmalee ES Addition & General Upgrades         Construction         96%         \$3,571,423         \$4,145,345         \$	\$55,780 \$20 \$55,617 \$3 \$10,749 \$28,829) \$3	03,716 35,165	PI
H DW HVAC 2020         Construction         100%         \$1,926,540         \$2,082,157         \$           2-ES 1-Other         Construction         100%         \$7,027,183         \$7,437,932         \$           H DW Network Upgrades         Construction         100%         \$7,027,183         \$7,437,932         \$           75-ES 13-MS 12-HS 18-Other         Construction         99%         \$6,403,971         \$6,375,141         (\$           Manning School Addition & General Upgrades         Construction         96%         \$3,571,423         \$4,145,345         \$	155,617 \$: 410,749 28,829) \$:	35,165	
2-ES 1-Other       Construction       100%       \$7,027,183       \$7,437,932       \$75-ES 13-MS 12-HS 18-Other         Manning School Addition & General Upgrades       Construction       99%       \$6,403,971       \$6,375,141       (\$7,027,183       \$7,437,932       \$7,	410,749 28,829) \$:		
75-ES 13-MS 12-HS 18-Other       Construction       99%       \$6,403,971       \$6,375,141       (\$9,403,971       \$6,375,141       \$6,375,141       \$6,375,141       \$6,375,141       \$6,375,141       \$6,375,142       \$	28,829) \$3	\$0	
Parmalee ES Addition & General Upgrades Construction 96% \$3,571,423 \$4,145,345 \$	-		
10	573,922 \$	29,972	
		40,777	SC
Pomona HS Addition & General Upgrades   Construction   93%   \$9,368,604   \$8,997,634   (\$3	70,969)	\$0	
Arvada K-8 Efficiency & Future Ready Close Out 100% \$2,094,864 \$1,957,848 (\$1	37,015) \$24	45,688	
Bell MS Addition & General Upgrades Close Out 99% \$6,877,348 \$6,948,052	\$70,704 \$8	38,323	
CTE South New Bldg Close Out 100% \$10,000,000 \$10,158,073 \$	158,073	\$0	
Charter Excel Academy Charter School General Upgrades Close Out 98% \$3,090,152 \$3,831,411 \$	741,259	\$0	PI
Charter Lincoln Academy Charter School General Upgrades Close Out 100% \$3,090,152 \$3,827,478 \$	737,326	\$0	PI
Conifer HS Addition & General Upgrades Close Out 100% \$7,550,789 \$10,460,106 \$2,	909,317	\$0	MC,UC,OB
Conifer HS FF&E Close Out 100% \$892,500 \$928,551	\$36,051	\$0	
	\$2,644)	\$0	
5, 10	360,236 \$1	75,482	
	164,746	\$0	
	78,864)	\$0	
		25,460	SC
	10,863)	\$0	
H DW Flooring 2020-I Close Out 100% \$600,430 \$642,980 2-ES 2-Other	\$42,550 \$4	47,252	
H DW Modular Bldg Removal 2020         Close Out         100%         \$0         \$445,637         \$           3-ES         3-ES         \$0 <t< td=""><td>145,637</td><td>\$0</td><td></td></t<>	145,637	\$0	
H DW Paving 2020-II 3-ES 1-Other Close Out 100% \$509,250 \$532,621	\$23,371	\$0	
H DW Playgrounds 2020 Close Out 100% \$1,051,742 \$1,372,625 \$ 8-ES 2-Other \$1,051,742	320,883	\$0	
H DW Roofing 2020-I 3-ES 1-Other Close Out 100% \$2,182,195 \$2,390,300 \$	208,105	\$0	
4-ES 1-MS 1-HS	66,466)	\$0	
Jefferson HS Addition & General UpgradesClose Out99%\$12,225,139\$12,225,139		41,668	
	44,740)	\$0	
	79,828) \$29	98,902	
Wayne Carle MS Addition & General Upgrades Close Out 97% \$5,201,180 \$4,850,545 (\$3	50,635)	\$0	
Adams ES Efficiency & Future Ready         Complete         100%         \$1,053,714         \$991,491         (\$	62,223)	\$0	
Arvada HS FF&E Complete 100% \$1,417,500 \$1,063,645 (\$3	53,855)	\$0	
Belmar ES Efficiency & Future + Paving         Complete         100%         \$690,210         \$848,999         \$	158,790 \$	35,281	
·	295,744	\$0	
	\$56,810	\$0	PI
Columbine Hills ES Efficiency & Future Ready Complete 100% \$820,608 \$1,030,910 \$	210,302 \$	18,306	
Coronado ES Efficiency & Future Ready         Complete         100%         \$2,377,700         \$2,211,237         (\$1	66,463) \$	11,023	
Coronado ES FF&E         Complete         100%         \$525,000         \$192,990         (\$3	32,010)	\$0	
Dutch Creek ES Efficiency & Future ReadyComplete100%\$1,101,361\$1,238,749	137,388 \$	38,240	
Dutch Creek ES FF&E         Complete         100%         \$472,500         \$146,847         (\$3	25,653)	\$0	
Eiber ES FF&E Complete 100% \$598,500 \$248,332 (\$3	50,168)	\$0	
Foothills ES Efficiency & Future Ready Complete 100% \$883,658 \$1,127,680 \$	244,022 \$	51,404	
Foothills ES FF&E Complete 100% \$378,000 \$137,254 (\$2	40,746)	\$0	
Fremont ES Efficiency & Future Ready Complete 100% \$1,038,912 \$1,087,700	\$48,788 \$10	02,186	
Green Gables ES Efficiency & Future Ready Complete 100% \$1,477,970 \$1,471,253	\$6,717) \$	71,513	
Green Gables ES FF&E         Complete         100%         \$399,000         \$95,144         (\$3	03,856)	\$0	

Report Date: 15-Mar-22 Page 5 of 11



Fiscal Plan Year: 2020	Work Pro	gress		Bu	dget Summar	у	
Project Description	Phase	%	Original	Current	Variance	Haz-Mat	Notes
H 581 Conference Place Reopen Phase 2	Complete	100%	\$0	\$506,698	\$506,698	\$0	UC,EC,SC
H DW Elevator Upgrades 3-ES 4-MS 3-HS 1-Other	Complete	100%	\$58,568	\$370,908	\$312,340	\$0	
H DW Flooring 2020-II 4-ES	Complete	100%	\$411,604	\$395,793	(\$15,811)	\$58,547	
H DW IT Cameras 2020 24-ES 7-MS 9-HS 16-Other	Complete	100%	\$878,600	\$862,398	(\$16,202)	\$0	
H DW LED Lighting - Interior 17-ES 1-Other	Complete	100%	\$2,781,920	\$2,881,698	\$99,778	\$31,522	
H DW Paving 2020-I 2-ES 1-MS	Complete	100%	\$225,750	\$311,775	\$86,025	\$0	
H DW Security Glass 2020-I 11-ES 1-Other	Complete	100%	\$88,000	\$52,125	(\$35,875)	\$7,829	
Hackberry Hill ES Efficiency & Future Ready	Complete	100%	\$708,508	\$551,787	(\$156,721)	\$0	
Hutchinson ES Efficiency & Future Ready	Complete	100%	\$1,954,477	\$1,770,012	(\$184,466)	\$89,801	
Hutchinson ES FF&E	Complete	100%	\$288,750	\$93,708	(\$195,042)	\$0	
Ken Caryl MS FACS CR + Bldg Signage	Complete	100%	\$343,200	\$374,447	\$31,247	\$22,608	
Lukas ES Efficiency & Future Ready	Complete	100%	\$1,106,650	\$1,147,495	\$40,845	\$0	
Lukas ES FF&E	Complete	100%	\$151,450	\$86,577	(\$64,873)	\$0	
Ralston ES Efficiency & Future Ready	Complete	100%	\$827,236	\$916,564	\$89,327	\$102,488	
Semper ES Efficiency & Future Ready	Complete	100%	\$1,540,562	\$1,582,813	\$42,251	\$0	
Stober ES Efficiency & Future Ready	Complete	100%	\$3,492,085	\$3,413,009	(\$79,076)	\$142,252	
Stober ES FF&E	Complete	100%	\$78,750	\$190,522	\$111,772	\$0	
Three Creeks K-8 FF&E	Complete	100%	\$0	\$194,960	\$194,960	\$0	
Trailblazer Stadium Efficiency & Future Ready	Complete	100%	\$4,415,250	\$4,275,888	(\$139,362)	\$0	
Vivian ES Efficiency & Future Ready	Complete	100%	\$1,506,673	\$1,752,143	\$245,470	\$116,661	
Welchester ES Efficiency & Future Ready	Complete	100%	\$1,407,615	\$1,726,787	\$319,172	\$60,146	
Welchester ES FF&E	Complete	100%	\$288,750	\$80,358	(\$208,392)	\$0	
West Jefferson MS Efficiency & Future Ready	Complete	100%	\$1,809,680	\$1,693,835	(\$115,845)	\$0	
Westridge ES HVAC	Complete	100%	\$780,720	\$1,536,383	\$755,663	\$0	OB,EC,SC
Wilmot ES FF&E	Complete	100%	\$304,500	\$347,176	\$42,676	\$0	
Witt ES Efficiency & Future Ready	Complete	100%	\$1,737,130	\$2,006,960	\$269,830	\$103,815	
Witt ES FF&E	Complete	100%	\$220,350	\$127,368	(\$92,982)	\$0	
	2020 Sub	totals:	\$164,465,729	\$185,714,637	\$18,402,881	\$2,846,027	

Fiscal Plan Year: 2019	Work Prog	ress	Budget Summary				
Project Description	Phase	%	Original	Current	Variance	Haz-Mat	Notes
H North Area Transportation-Joyce Renovation	Design	53%	\$349,400	\$568,227	\$218,827	\$0	
Alameda HS Addition & General Upgrades	Construction	89%	\$19,055,745	\$29,882,228	\$10,826,483	\$0	UC,SC
Alameda Int'l Jr-Sr Asbestos Abatement	Construction	46%	\$0	\$0	\$0	\$1,641,966	
Charter Collegiate Academy of Colorado General Upgrades	Construction	86%	\$3,090,152	\$3,831,451	\$741,299	\$0	PI
Charter Mountain Phoenix Community School General Upgrad	Construction	85%	\$3,090,152	\$3,826,667	\$736,515	\$0	PI
H DW FF&E Allocation	Construction	100%	\$0	\$44,956	\$44,956	\$0	
West Jefferson MS FF&E	Construction	92%	\$395,000	\$395,225	\$225	\$0	
Arvada HS Addition & General Upgrades	Close Out	100%	\$12,018,096	\$15,234,824	\$3,216,728	\$222,010	UC,OB,EC
Charter Addenbrooke Classical Academy General Upgrades	Close Out	100%	\$3,090,152	\$3,828,963	\$738,811	\$0	PI
Columbine HS Addition & General Upgrades	Close Out	100%	\$11,482,013	\$17,863,827	\$6,381,814	\$272,854	UC,SC,OB
Green Mountain HS Addition & General Upgrades	Close Out	100%	\$11,105,728	\$12,168,946	\$1,063,217	\$70,021	MC,UC,SC
Kendrick Lakes ES Replace School	Close Out	100%	\$22,743,115	\$20,228,748	(\$2,514,367)	\$181,141	MC
Pomona HS FF&E	Close Out	100%	\$0	\$90,910	\$90,910	\$0	
Wilmot ES Addition & General Upgrades	Close Out	100%	\$3,212,843	\$8,164,168	\$4,951,325	\$95,628	MC,UC,OB
Adams ES FF&E	Complete	100%	\$324,450	\$155,779	(\$168,671)	\$0	
Arvada K8 FF&E	Complete	100%	\$0	\$709,697	\$709,697	\$0	19M
Charter-Compass Montessori Golden Debt Repayment	Complete	100%	\$3,090,152	\$4,246,502	\$1,156,350	\$0	CC
Charter-Jefferson Acad. Secondary Addition	Complete	100%	\$6,180,304	\$6,213,940	\$33,636	\$0	CC,PI
Charter-Rocky Mtn Acad. Evergreen Debt Repayment	Complete	100%	\$3,090,152	\$3,101,864	\$11,712	\$0	PI
Charter-Two Roads Arvada Debt Repayment	Complete	100%	\$3,090,152	\$3,104,376	\$14,224	\$0	PI

Report Date: 15-Mar-22 Page 6 of 11



Fiscal Plan Year: 2019	Work Pro	gress		Bu	dget Summary			
Project Description	Phase	%	Original	Current	Variance	Haz-Mat	Notes	
Charter-Woodrow Wilson Academy Debt Repayment	Complete	100%	\$3,090,152	\$3,101,768	\$11,616	\$0	PI	
Creighton MS FF&E	Complete	100%	\$0	\$162,251	\$162,251	\$0		
Evergreen HS Storm Drain Repair	Complete	100%	\$0	\$389,281	\$389,281	\$0		
Everitt MS Library Renovation	Complete	100%	\$545,789	\$545,789	\$0	\$0		
H DW Building Lighting 1-MS	Complete	100%	\$299,775	\$946,487	\$646,712	\$0	19M	
H DW Curtain Riggings 8-HS	Complete	100%	\$0	\$173,922	\$173,922	\$0		
H DW Field Improvements 1-MS 7-HS	Complete	100%	\$12,157,500	\$20,327,403	\$8,169,903	\$0	SC,19M	
H DW Fire Alarms 1-ES 1-MS 1-HS 1-Other	Complete	100%	\$64,877	\$177,130	\$112,254	\$0		
H DW Flooring 12-ES 4-Other	Complete	100%	\$886,851	\$1,563,346	\$676,495	\$321,861	19M	
H DW Gym Divider Curtains 6-MS 1-Other	Complete	100%	\$0	\$336,487	\$336,487	\$0		
1 DW HVAC 2-MS	Complete	100%	\$185,913	\$1,500,354	\$1,314,441	\$0	19M	
H DW IT Cameras 51-ES 1-HS 2-Other	Complete	100%	\$774,304	\$665,351	(\$108,953)	\$0		
H DW Irrigation 2-ES 1-MS 2-HS	Complete	100%	\$0	\$513,353	\$513,353	\$0	19M	
H DW Modular Bldg Removal 8-ES 1-MS 2-Other	Complete	100%	\$0	\$408,390	\$408,390	\$0		
H DW Paving 6-ES 1-MS 2-Other	Complete	100%	\$799,050	\$1,645,759	\$846,709	\$0	19M	
H DW Playgrounds 4-ES 4-Other	Complete	100%	\$873,810	\$1,566,807	\$692,997	\$0	19M	
H DW Roofing 3-ES 1-HS	Complete	100%	\$2,504,598	\$4,139,927	\$1,635,329	\$0	SC	
HDW Security Glass 9-ES	Complete	100%	\$67,997	\$43,303	(\$24,694)	\$6,504		
H DW Site Lighting 4-ES 2-Other	Complete	100%	\$130,000	\$807,114	\$677,114	\$0	19M	
H North Area Transportation-Joyce Site Acquisition	Complete	100%	\$7,000,600	\$7,000,600	\$0	\$0		
Ken Caryl MS FF&E	Complete	100%	\$0	\$188,133	\$188,133	\$0		
Ralston Valley HS Roofing	Complete	100%	\$0	\$1,670,244	\$1,670,244	\$0	19M	
Summit Ridge MS FF&E	Complete	100%	\$0	\$192,838	\$192,838	\$0		
Three Creeks K-8 Addition & General Upgrades	Complete	100%	\$4,931,850	\$5,664,653	\$732,803	\$0	MC,OB	
	2019 Sub	ototals:	\$139,720,671	\$190,203,974	\$47,671,318	\$2,811,985		

Report Date: 15-Mar-22 Page 7 of 11



#### **Report Reference**

#### Work Progress Columns:

Phase The current phase of the project life cycle as most recently reported by the project

manager

% An estimate of payable work progress calculated from the latest status and

forecast in the project management system

## **Budget Summary Columns:**

Original The original estimated budget for the project scope

Current The latest revised budget including all approved changes Variance The difference between the Original and Current budget

Haz-Mat Additional budget approved for hazardous materials mitigation

Notes Abbreviated variance descriptions for projects with significant budget Variance

(see translation table below)

#### Variance Notes

Note	Description
MC	Market Conditions
UC	Unforeseen Conditions
SC	Scope Change
19M	19M Program Scope - Initial project budget did not cover hazardous materials. If hazardous materials were identified it was paid out of program contingency.
PI	Premium and Interest Earned by Charter
ОВ	Occupied Building
EC	Existing Conditions
CC	Budget Shared Between Charter Campuses
FFE	Additional Fixtures, Furnishings and Equipment (FF&E) scope identified through a full assessment by the FF&E team. This team was not in place until after the initial bond program development.
DB	Directed by the Board of Education

Report Date: 15-Mar-22 Page 8 of 11



## Facility Listings for Multi-Site (DW) Projects

Fiscal Plan Year: 2022			
Project Description	Project Facilities		
G DW Modular Bldg Removal 2022 7-ES 1-Other	Glennon Heights ES, Governor's Ranch ES, Lasley ES, Little ES, Molholm ES, South Lakewood ES, Westgate ES, Brady Exploration School		
G DW Elevator Upgrades 2022 1-ES 1-MS 1-HS	Peck ES, Deer Creek MS, Golden HS		
G DW LED Lighting 2022 8-ES 2-MS 2-HS 3-Other	Bradford K-8 South, Bradford K-8 North, Lawrence ES, Leawood ES, Meiklejohn ES, Normandy ES, Rooney Ranch ES, Ute Meadows ES, Weber ES, West Woods ES, Brady Exploration School, Creighton MS, Moore MS, Chatfield HS, Dakota Ridge HS		
G DW Paving 2022 5-ES 1-MS	Campbell ES, Little ES, Peiffer ES, South Lakewood ES, Thomson ES, Falcon Bluffs MS		
G DW Flooring 2022-I 4-ES 3-MS	Governor's Ranch ES, Mount Carbon ES, Peiffer ES, Rooney Ranch ES, Deer Creek MS, Falcon Bluffs MS, Summit Ridge MS		
G DW Playground 2022-I 4-ES	Glennon Heights ES, Governor's Ranch ES, Mount Carbon ES, Peiffer ES		
G DW Flooring 2022-II 7-ES	Glennon Heights ES, Little ES, Parr ES, Pennington ES, South Lakewood ES, Swanson ES, Van Arsdale ES		
G DW Mechanical 2022 3-ES	Campbell ES, Little ES, Van Arsdale ES		
G DW Network Upgrades 2022 75-ES 13-MS 12-HS 18-Other	Allendale ES, Adams ES, Arvada K-8, Bear Creek K-8, Blue Heron ES, Belmar School of Integrated Arts, Campbell ES, Bradford K-8 North, Colorow ES, Coal Creek Canyon K-8, Columbine Hills ES, Coronado ES, Devinny ES, Dutch Creek ES, Edgewater ES, Eiber ES, Emory ES, Fairmount ES, Fitzmorris ES, Foothills ES, Foster ES, Fremont ES, Anderson Preschool, Glennon Heights ES, Governor's Ranch ES, Green Gables ES, Green Mountain ES, Hackberry Hill ES, Hutchinson ES, Irwin Preschool, Sheridan Green ES, Kendallvue ES, Kullerstrand ES, Kyffin ES, Lasley ES, Lawrence ES, Leawood ES, Little ES, Lukas ES, Lumberg ES, Maple Grove ES, Meiklejohn ES, Mitchell ES, Molholm ES, Mortenson ES, Mount Carbon ES, Normandy ES, Parr ES, Patterson International School, Pennington ES, Peck ES, Peiffer ES, Powderhorn ES, Red Rocks ES, Rooney Ranch ES, Stott ES, Ryan ES, Secrest ES, Semper ES, Shaffer ES, Shelton ES, Sierra ES, Slater ES, Deane ES, South Lakewood ES, Stober ES, Stevens ES, Swanson ES, Stony Creek ES, Litz Preschool, Thomson ES, Vanderhoof ES, Van Arsdale ES, Ute Meadows ES, Vivian ES, Warder ES, Weber ES, Welchester ES, Westgate ES, Westridge ES, West Woods ES, Wilmore Davis ES, Witt ES, Brady Exploration School, Dennison ES, Manning School, McLain Community HS, Jeffco Open School, Miller Special School, Free Horizon Montessori (Charter), Warren Tech Central, Long View HS, Bell MS, Wayne Carle MS, Carmody MS, Creighton MS, Deer Creek MS, Drake MS, Dunstan MS, Everitt MS, Falcon Bluffs MS, Mandalay MS, Moore MS, Oberon MS, North Arvada MS, Wheat Ridge 5-8, Arvada HS, Bear Creek HS, Chatfield HS, Dakota Ridge HS, Golden HS, Jefferson Jr-Sr HS, Lakewood HS, Pomona HS, Ralston Valley HS, Standley Lake HS, Wheat Ridge HS, Connections Learning Center		
G DW Playground 2022-II 2-ES	Campbell ES, Fairmount ES		
G DW Roofing 2022 4-ES 1-MS	Campbell ES, Fairmount ES, Pennington ES, South Lakewood ES, Summit Ridge MS		
G DW Security Glass 2022 7-ES 1-MS 1-HS 1-Other	Bear Creek K-8, Campbell ES, Fairmount ES, Little ES, Parr ES, Pennington ES, South Lakewood ES, Swanson ES, Summit Ridge MS, Arvada West HS		

Fiscal Plan Year: 2021			
Project Description	Project Facilities		
G DW Field Improvements 2021 1-ES 4-HS	Lumberg ES, D'Evelyn Jr-Sr HS, Alameda Int'l Jr-Sr HS, Jefferson Jr-Sr HS, Wheat Ridge HS		
G DW LED Lighting 2021 11-ES	Edgewater ES, Elk Creek ES, Emory ES, Kyffin ES, Red Rocks ES, Shaffer ES, Stevens ES, Stony Creek ES, Thomson ES, Warder ES, West Jefferson ES		
G DW Mechanical 2021 5-ES	Edgewater ES, Elk Creek ES, Peck ES, Secrest ES, Thomson ES		
H DW Elevator Upgrades 2021 6-ES 7-MS 8-HS 4-Other	Bear Creek K-8, Emory ES, Lawrence ES, Meiklejohn ES, Peck ES, Stevens ES, Wilmot ES, Free Horizon Montessori (Charter), Warren Tech North, Warren Tech South, Wayne Carle MS, Carmody MS, Creighton MS, Dunstan MS, Falcon Bluffs MS, Summit Ridge MS, North Arvada MS, Alameda Int'l Jr-Sr HS, Bear Creek HS, Chatfield HS, Golden HS, Jefferson Jr-Sr HS, Lakewood HS, Ralston Valley HS, Wheat Ridge HS		
G DW Flooring 2021 6-ES	Emory ES, Peck ES, Red Rocks ES, Shaffer ES, Thomson ES, Westgate ES		
G DW Modular Bldg Removal 2021 5-ES	Kendallvue ES, Kullerstrand ES, Lawrence ES, Slater ES, Vivian ES		

Report Date: 15-Mar-22 Page 9 of 11



Fiscal Plan Year: 2021			
Project Description	Project Facilities		
G DW Paving 2021 3-ES 1-MS	Parmalee ES, Red Rocks ES, West Jefferson ES, Ken Caryl MS		
G DW Playgrounds 2021 9-ES	Elk Creek ES, Kyffin ES, Normandy ES, Peck ES, Red Rocks ES, Secrest ES, Shaffer ES, Thomson ES, Warder ES		
G DW Roofing 2021 5-ES	Emory ES, Fitzmorris ES, Lawrence ES, Stevens ES, Westgate ES		
G DW Security Glass 2021 6-ES 5-MS 1-HS	Dutch Creek ES, Leawood ES, Meiklejohn ES, Red Rocks ES, Rose Stein International ES, Weber ES, Ken Caryl MS, Creighton MS, Drake MS, Mandalay MS, Moore MS, Conifer HS		

Fiscal Plan Year: 2020	
Project Description	Project Facilities
H DW HVAC 2020 2-ES 1-Other	Patterson International School, Stott ES, Ryan ES
H DW Network Upgrades 75-ES 13-MS 12-HS 18-Other	Allendale ES, Adams ES, Arvada K-8, Bear Creek K-8, Blue Heron ES, Belmar School of Integrated Arts, Campbell ES, Bradford K-8 North, Colorow ES, Coal Creek Canyon K-8, Columbine Hills ES, Coronado ES, Devinny ES, Dutch Creek ES, Edgewater ES, Eiber ES, Emory ES, Fairmount ES, Fitzmorris ES, Foothills ES, Foster ES, Fremont ES, Anderson Preschool, Glennon Heights ES, Governor's Ranch ES, Green Gables ES, Green Mountain ES, Hackberry Hill ES, Hutchinson ES, Irwin Preschool, Sheridan Green ES, Kendallvue ES, Kullerstrand ES, Kyffin ES, Lasley ES, Lawrence ES, Leawood ES, Little ES, Lukas ES, Lumberg ES, Maple Grove ES, Meiklejohn ES, Mitchell ES, Molholm ES, Mortenson ES, Mount Carbon ES, Normandy ES, Parr ES, Patterson International School, Pennington ES, Peck ES, Peiffer ES, Powderhorn ES, Red Rocks ES, Rooney Ranch ES, Stott ES, Ryan ES, Secrest ES, Semper ES, Shaffer ES, Shelton ES, Sierra ES, Slater ES, Deane ES, South Lakewood ES, Stober ES, Stevens ES, Swanson ES, Stony Creek ES, Litz Preschool, Thomson ES, Vanderhoof ES, Van Arsdale ES, Ute Meadows ES, Vivian ES, Warder ES, Weber ES, Welchester ES, Westgate ES, Westridge ES, West Woods ES, Wilmore Davis ES, Witt ES, Brady Exploration School, Dennison ES, Manning School, McLain Community HS, Jeffco Open School, Miller Special School, Free Horizon Montessori (Charter), Warren Tech Central, Long View HS, Bell MS, Wayne Carle MS, Carmody MS, Creighton MS, Deer Creek MS, Drake MS, Dunstan MS, Everitt MS, Falcon Bluffs MS, Mandalay MS, Moore MS, Oberon MS, North Arvada MS, Wheat Ridge 5-8, Arvada HS, Bear Creek HS, Chatfield HS, Dakota Ridge HS, Golden HS, Jefferson Jr-Sr HS, Lakewood HS, Pomona HS, Ralston Valley HS, Standley Lake HS, Wheat Ridge HS, Connections Learning Center
H DW Field Improvements 11-HS	Arvada HS, Arvada West HS, Chatfield HS, Columbine HS, Conifer HS, Dakota Ridge HS, Golden HS, Green Mountain HS, Lakewood HS, Pomona HS, Standley Lake HS
H DW Fire Sprinklers Replacement 3-ES 1-MS 1-Other	Bradford K-8 North, Rooney Ranch ES, Ryan ES, Van Arsdale ES, Deer Creek MS
H DW Flooring 2020-I 2-ES 2-Other	Fitzmorris ES, Lasley ES, Free Horizon Montessori (Formerly Pleasant View ES), Miller Special School
H DW Modular Bldg Removal 2020 3-ES	Campbell ES, Green Gables ES, Peck ES
H DW Paving 2020-II 3-ES 1-Other	Bradford K-8 North, Mitchell ES, Ryan ES, Shelton ES
H DW Playgrounds 2020 8-ES 2-Other	Allendale ES, Columbine Hills ES, Sheridan Green ES, Kendallvue ES, Free Horizon Montessori (Formerly Pleasant View ES), Stott ES, Stony Creek ES, Vanderhoof ES, Westridge ES, Miller Special School
H DW Roofing 2020-I 3-ES 1-Other	Green Mountain ES, Lasley ES, Parr ES, Patterson International School
H DW Roofing 2020-II 4-ES 1-MS 1-HS	Kullerstrand ES, Little ES, Swanson ES, Thomson ES, Carmody MS, Evergreen HS
H DW Elevator Upgrades 3-ES 4-MS 3-HS 1-Other	Lawrence ES, Peck ES, Wilmot ES, Carmody MS, Creighton MS, Deer Creek MS, Falcon Bluffs MS, Bear Creek HS, Conifer HS, Dakota Ridge HS, Education Service Center
H DW Flooring 2020-II 4-ES	Allendale ES, Fairmount ES, Thomson ES, West Woods ES
H DW IT Cameras 2020 24-ES 7-MS 9-HS 16-Other	Allendale ES, Arvada K-8, Bear Creek K-8, Belmar School of Integrated Arts, Bradford K-8 South, Campbell ES, Bradford K-8 North, Coal Creek Canyon K-8, Coronado ES, Elk Creek ES, Fairmount ES, Fremont ES, Glennon Heights ES, Irwin Preschool, Meiklejohn ES, Mitchell ES, Mortenson ES, Ralston ES, Stott ES, Shaffer ES, Shelton ES, Slater ES, South Lakewood ES, Stony Creek ES, Litz Preschool, Vanderhoof ES, Van Arsdale ES, Ute Meadows ES, Welchester ES, West Jefferson ES, West Woods ES, Brady Exploration School, Dennison ES, Manning School, McLain Community HS, Jeffco Open School, Miller Special School, Warren Tech Central, Warren Tech North, Deer Creek MS, Evergreen MS, Everitt MS, Falcon Bluffs MS, Mandalay MS, Oberon MS, North Arvada MS, Alameda Int'l Jr-Sr HS, Arvada HS, Bear Creek HS, Evergreen HS, Jefferson Jr-Sr HS, Pomona HS, Ralston Valley HS, Standley Lake HS, Wheat Ridge HS, Connections Learning Center
H DW LED Lighting - Interior 17-ES 1-Other	Columbine Hills ES, Devinny ES, Fitzmorris ES, Sheridan Green ES, Kullerstrand ES, Lasley ES, Maple Grove ES, Patterson International School, Peck ES, Powderhorn ES, Stott ES, Ryan ES, Secrest ES, Deane ES, Vanderhoof ES, Westgate ES, Westridge ES, Dennison ES

Report Date: 15-Mar-22 Page 10 of 11



Fiscal Plan Year: 2020	
Project Description	Project Facilities
H DW Paving 2020-I 2-ES 1-MS	Columbine Hills ES, Lawrence ES, Everitt MS
H DW Security Glass 2020-I 11-ES 1-Other	Elk Creek ES, Green Mountain ES, Kyffin ES, Mitchell ES, Peck ES, Secrest ES, Shelton ES, Slater ES, Stevens ES, Thomson ES, Warder ES, Wheat Ridge 5-8


Fiscal Plan Year: 2019			
Project Description	Project Facilities		
H DW FF&E Allocation			
H DW Building Lighting 1-MS	North Arvada MS		
H DW Curtain Riggings 8-HS	Alameda Int'l Jr-Sr HS, Arvada West HS, Bear Creek HS, Evergreen HS, Golden HS, Lakewood HS, Pomona HS, Wheat Ridge HS		
H DW Field Improvements 1-MS 7-HS	West Jefferson MS, Arvada HS, Chatfield HS, Conifer HS, Dakota Ridge HS, Evergreen HS, Lakewood HS, Ralston Valley HS		
H DW Fire Alarms 1-ES 1-MS 1-HS 1-Other	Red Rocks ES, D'Evelyn Jr-Sr HS, Mandalay MS, 809 Bldg 1 Service Center Bldg 1		
H DW Flooring 12-ES 4-Other	Bergen Meadow ES, Bradford K-8 South, Bradford K-8 North, Eiber ES, Foothills ES, Green Mountain ES, Hutchinson ES, Sheridan Green ES, Kullerstrand ES, Lukas ES, Free Horizon Montessori (Formerly Pleasant View ES), Vivian ES, Welchester ES, Westridge ES, Wilmore Davis ES, Free Horizon Montessori (Charter)		
H DW Gym Divider Curtains 6-MS 1-Other	Manning School, Ken Caryl MS, Carmody MS, Drake MS, Everitt MS, Oberon MS, North Arvada MS		
H DW HVAC 2-MS	Bell MS, Drake MS		
H DW IT Cameras 51-ES 1-HS 2-Other	Adams ES, Blue Heron ES, Bergen Valley ES, Bergen Meadow ES, Colorow ES, Columbine Hills ES, Devinny ES, Dutch Creek ES, Edgewater ES, Fitzmorris ES, Foothills ES, Foster ES, Governor's Ranch ES, Green Gables ES, Green Mountain ES, Hackberry Hill ES, Hutchinson ES, Sheridan Green ES, Kendallvue ES, Kullerstrand ES, Lasley ES, Lawrence ES, Leawood ES, Little ES, Lukas ES, Lumberg ES, Molholm ES, Mount Carbon ES, Normandy ES, Parr ES, Parmalee ES, Patterson International School, Pennington ES, Peck ES, Peiffer ES, Powderhorn ES, Red Rocks ES, Ronney Ranch ES, Ryan ES, Secrest ES, Semper ES, Deane ES, Rose Stein International ES, Stober ES, Swanson ES, Thomson ES, Vivian ES, Warder ES, Westgate ES, Westridge ES, Wilmore Davis ES, Wilmot ES, Free Horizon Montessori (Charter), Columbine HS		
H DW Irrigation 2-ES 1-MS 2-HS	Colorow ES, Deane ES, D'Evelyn Jr-Sr HS, Evergreen MS, Pomona HS		
H DW Modular Bldg Removal 8-ES 1-MS 2-Other	Campbell ES, Fremont ES, Green Gables ES, Peck ES, Peiffer ES, Swanson ES, Stony Creek ES, Westridge ES, Miller Special School, Warren Tech Central, Carmody MS		
H DW Paving 6-ES 1-MS 2-Other	Bradford K-8 South, Bradford K-8 North, Devinny ES, Fitzmorris ES, Hackberry Hill ES, Maple Grove ES, Peck ES, Ryan ES, Evergreen MS		
H DW Playgrounds 4-ES 4-Other	Belmar School of Integrated Arts, Columbine Hills ES, Patterson International School, Free Horizon Montessori (Formerly Pleasant View ES), Ralston ES, Welchester ES, Wilmore Davis ES, Free Horizon Montessori (Charter)		
H DW Roofing 3-ES 1-HS	Eiber ES, Green Gables ES, Wilmot ES, Lakewood HS		
H DW Security Glass 9-ES	Allendale ES, Devinny ES, Sheridan Green ES, Lawrence ES, Stott ES, Ryan ES, Vanderhoof ES, Westridge ES, Dennison ES		
H DW Site Lighting 4-ES 2-Other	Belmar School of Integrated Arts, Eiber ES, Foothills ES, Ralston ES, Welchester ES, 809 Campus Service Center Campus		

Report Date: 15-Mar-22 Page 11 of 11



# 23M Capital Program 2023-24

## **Program Dollar Value by Phase**

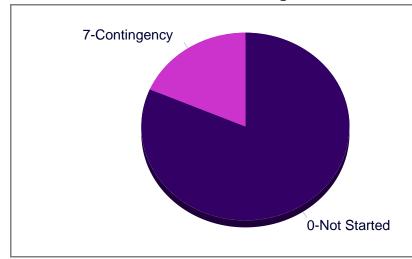

Project Phase	Project Count	Dollar Value
0-Not Started	2	\$650,000
1-Design	0	\$0
2-Bid-Award	0	\$0
3-Construction	0	\$0
4-Close Out	0	\$0
5-Complete	0	\$0
6-On Hold	0	\$0
7-Contingency	1	\$147,852
Totals	3	\$797,852

## **Program Narrative**

The 23M Capital Program represents Fiscal Year 2023 planned projects that are expected to complete in Fiscal Year 2024. These projects are reviewed by the Capital Asset Advisory Committee.

Occupancy Deadlines At Risk			Finisl	h Date	
Priority	Facility Name	Project ID	Project name	Target	Forecast

## **Program Contingency and Remaining Funds**

Program Contingency (Unallocated)	Forecast Remaining Funds in Projects	Net Remaining Program Funds
\$147,852	\$0	\$147,852

Report Date: 15-Mar-22 Page 1 of 8



# 23M Capital Program 2023-24 - Project Detail


	Work Prog	ress		
Project Description	Phase	%	Capital Budget	Other Funding Sources
23M Meyers Pool Parking Lot	Not Started	0%	\$50,000	\$0
23M Wheat Ridge HS Replace Field Turf	Not Started	0%	\$600,000	\$0
23M Program Contingency	Contingency	0%	\$147,852	\$0
	Program	Totals:	\$797,852	\$0

Report Date: 15-Mar-22 Page 2 of 8



## 22M Capital Program 2022-23

## **Program Dollar Value by Phase**

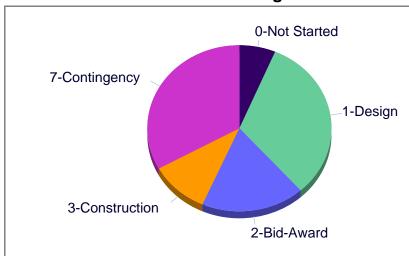

	B	
Duningt Dhann	Project	Dallar Value
Project Phase	Count	Dollar Value
0-Not Started	3	\$210,000
1-Design	7	\$1,062,429
2-Bid-Award	1	\$600,000
3-Construction	5	\$343,579
4-Close Out	0	\$0
5-Complete	0	\$0
6-On Hold	0	\$0
7-Contingency	1	\$1,093,992
Totals	17	\$3,310,000

## **Program Narrative**

The 22M Capital Program represents Fiscal Year 2022 planned projects that are expected to complete in Fiscal Year 2023. These projects are reviewed by the Capital Asset Advisory Committee.

00	Occupancy Deadlines At Risk			n Date
Priority Facility Name	Project ID	Project name	Target	Forecast

## **Program Contingency and Remaining Funds**

Program Contingency	Forecast Remaining	Net Remaining
(Unallocated)	Funds in Projects	Program Funds
\$1,093,992	(\$91,550)	\$1,002,442

Report Date: 15-Mar-22 Page 3 of 8



# 22M Capital Program 2022-23 - Project Detail


	Work Prog	ress		
Project Description	Phase	%	Capital Budget	Other Funding Sources
22M DW Planning & Design Allocation	Not Started	16%	\$200,000	\$0
22M DW Small Projects 2 Allocation	Not Started	0%	\$10,000	\$0
22M Green Gables ES Walking Path	Not Started	0%	\$0	\$0
22M Arvada HS Irv Brown Center	Design	100%	\$15,000	\$0
22M D'Evelyn Jr/Sr FF&E	Design	1%	\$118,320	\$0
22M DW Property Disposal Allocation	Design	100%	\$24,600	\$0
22M DW Small Projects 1 Allocation	Design	26%	\$508,019	\$62,858
22M DW Temp Bldg Lease Allocation	Design	76%	\$96,490	\$0
22M DW Utilization Allocation	Design	42%	\$150,000	\$0
22M DW Water Engineering Allocation	Design	32%	\$150,000	\$0
22M Bear Creek HS Replace Field Turf	Bid-Award	0%	\$600,000	\$0
22M Columbine HS Drainage Improvements	Construction	3%	\$82,140	\$0
22M DW FF&E Allocation	Construction	20%	\$45,000	\$0
22M DW HVAC UV Lighting Pilot	Construction	89%	\$115,432	\$0
22M Stober ES Garden-Outdoor Classroom	Construction	0%	\$0	\$61,616
22M Welchester ES Kitchen	Construction	12%	\$101,008	\$85,981
22M DW Program Contingency	Contingency	0%	\$1,093,992	\$0
	Program	Totals:	\$3,310,000	\$210,455

Report Date: 15-Mar-22 Page 4 of 8



## 21M Capital Program 2021-22

## **Program Dollar Value by Phase**

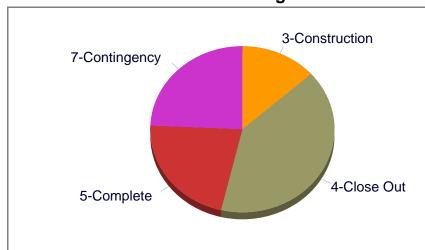

Project Phase	Project Count	Dollar Value
0-Not Started	0	\$0
1-Design	0	\$0
2-Bid-Award	0	\$0
3-Construction	4	\$428,484
4-Close Out	14	\$1,286,843
5-Complete	3	\$701,346
6-On Hold	0	\$0
7-Contingency	1	\$775,244
Totals	22	\$3,191,917

## **Program Narrative**

The 21M Capital Program represents Fiscal Year 2021 planned projects that are expected to complete in Fiscal Year 2022. These projects are reviewed by the Capital Asset Advisory Committee.

00	Occupancy Deadlines At Risk			n Date
Priority Facility Name	Project ID	Project name	Target	Forecast

## **Program Contingency and Remaining Funds**

Program Contingency (Unallocated)	Forecast Remaining Funds in Projects	Net Remaining Program Funds
\$775,244	\$14,017	\$789,261

Report Date: 15-Mar-22 Page 5 of 8



# 21M Capital Program 2021-22 - Project Detail


	Work Prog	ress		
Project Description	Phase	%	Capital Budget	Other Funding Sources
21M Alameda HS School Funded Add-Ons	Construction	21%	\$25,000	\$82,398
21M 5th Floor Data Center Improvements	Construction	84%	\$21,245	\$655,397
21M Alameda Intl Kitchen-Cafeteria Renovation	Construction	93%	\$61,862	\$600,000
21M DW Reservoir Measuring Systems	Construction	32%	\$320,377	\$0
21M Candelas Regional Trail	Close Out	100%	\$212,338	\$0
21M Columbine HS School-Funded Add-On Scope	Close Out	100%	\$79,738	\$284,474
21M Conifer HS FF&E	Close Out	100%	\$50,000	\$0
21M D'Evelyn Jr-Sr HS Roofing	Close Out	100%	\$257,512	\$0
21M DW Energy Conservation Allocation	Close Out	100%	\$18,426	\$0
21M DW Field Net Systems	Close Out	100%	\$120,341	\$0
21M DW Planning & Design Allocation	Close Out	100%	\$92,016	\$0
21M DW Property Disposal Allocation	Close Out	100%	\$855	\$0
21M DW Small Projects 2 Allocation	Close Out	100%	\$96,168	\$0
21M DW Temp. Bldg. Lease Allocation	Close Out	100%	\$96,490	\$0
21M DW Utilization Allocation	Close Out	100%	\$57,183	\$0
21M DW Water Engineering Allocation	Close Out	100%	\$136,062	\$0
21M Green Mountain HS Corridor Flooring	Close Out	100%	\$50,000	\$0
21M Jeffco Open School Playground	Close Out	100%	\$19,714	\$100,800
21M 809 Bldg 1 Security Dispatch System	Complete	100%	\$144,600	\$49,000
21M DW Pilot-HVAC UV Lighting	Complete	100%	\$43,360	\$0
21M DW Small Projects 1 Allocation	Complete	100%	\$513,386	\$0
21M Program Contingency	Contingency	0%	\$775,244	\$0
	Program	Totals:	\$3,191,917	\$1,772,069

Report Date: 15-Mar-22 Page 6 of 8



## 20M Capital Program 2020-21

## **Program Dollar Value by Phase**

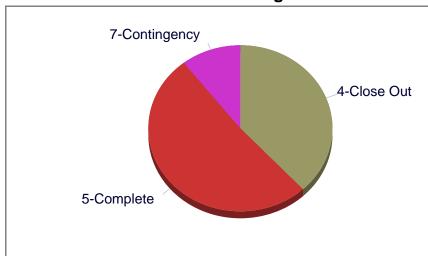

Project Phase	Project Count	Dollar Value
0-Not Started	0	\$0
1-Design	0	\$0
2-Bid-Award	0	\$0
3-Construction	0	\$0
4-Close Out	5	\$1,563,948
5-Complete	11	\$2,106,325
6-On Hold	0	\$0
7-Contingency	1	\$432,660
Totals	17	\$4,102,933

## **Program Narrative**

The 20M Capital Program 2020 -2021 represents Fiscal Year 2020 planned projects that are expected to complete in Fiscal Year 2021. These projects are reviewed by the Capital Asset Advisory Committee.

	Occupancy Deadlines At Risk				Finish Date	
Priority	Facility Name	Project ID	Project name	Target	Forecast	

## **Program Contingency and Remaining Funds**

Program Contingency (Unallocated)	Forecast Remaining Funds in Projects	Net Remaining Program Funds
\$432,660	\$0	\$432,660

Report Date: 15-Mar-22 Page 7 of 8



# 20M Capital Program 2020-21 - Project Detail

	Work Prog	ress		
Project Description	Phase	%	Capital Budget	Other Funding Sources
20M Alameda Int'l HS Auditorium Renovation	Close Out	100%	\$279,674	\$276,498
20M D'Evelyn Jr-Sr HS Utilities for Temps	Close Out	100%	\$638,829	\$0
20M DW Planning & Design Allocation	Close Out	100%	\$183,394	\$0
20M DW Tractor Sheds	Close Out	100%	\$215,346	\$0
20M Parmalee ES School Zone Enhancements	Close Out	99%	\$246,704	\$0
20M 581 Conf Place Solar Panel Purchase	Complete	100%	\$320,352	\$0
20M 809 Campus Fabric Storage Shelter	Complete	100%	\$62,600	\$0
20M Applewood Cottages Offices for EAP	Complete	100%	\$288,825	\$0
20M DW Property Disposal Allocation	Complete	0%	\$0	\$0
20M DW Small Projects 1 Allocation	Complete	100%	\$447,355	\$0
20M DW Small Projects 2 Allocation	Complete	100%	\$103,795	\$0
20M DW Temp. Bldg. Lease Allocation	Complete	100%	\$96,490	\$0
20M DW Utilization Allocation	Complete	100%	\$121,859	\$0
20M DW Water Engineering Allocation	Complete	100%	\$7,522	\$0
20M Free Horizon Montessori RTU Repair	Complete	100%	\$147,187	\$0
20M Golden HS Chiller Replacement	Complete	100%	\$510,339	\$0
20M Program Contingency	Contingency	0%	\$432,660	\$0
	Program	Totals:	\$4,102,933	\$276,498

Report Date: 15-Mar-22 Page 8 of 8

# Department of Construction Management Program Financial Summary Report



Date: Mar 16, 2022

Progi	ram	P	Program Contingency (Unallocated)	Forecast Remaining Funds in Projects	Net Remaining Program Funds
H/G	2018 Capital Improvement Plan		\$64,761,285	(\$7,655,618)	\$57,105,667
23M	23M Mini Program 2023-24		\$147,852	\$0	\$147,852
22M	22M Mini Program 2022-23		\$1,093,992	(\$91,550)	\$1,002,442
21M	21M Mini Program 2021-22		\$775,244	\$14,017	\$789,261
20M	20M Mini Program 2020-21		\$432,660	\$0	\$432,660
		Total:	\$67,211,033	(\$7,733,151)	\$59,477,882

Page **1 of 1** Report M\_JEFFCO\_COS\_11
